

Five days in, seven of nine phases done

The pilot build is running roughly four to five times ahead of its 30-day plan. The significant news is not the pace — it is that **the critical path has already moved off engineering**. What now stands between this build and a launch is a set of decisions and approvals that only AVO and its counsel can make.

Day 5 of 30


16–20 August 2026

Prepared for the project manager

CALENDAR USED 5 / 30 17% of the schedule	PHASES COMPLETE 7 / 9 78% of planned scope	AUTOMATED TESTS 889 passing, 0 failing	BLOCKED ON CLIENT 14 decisions awaiting AVO
---	---	---	--

SCOPE AGAINST CALENDAR


78% of the plan delivered in 17% of the time

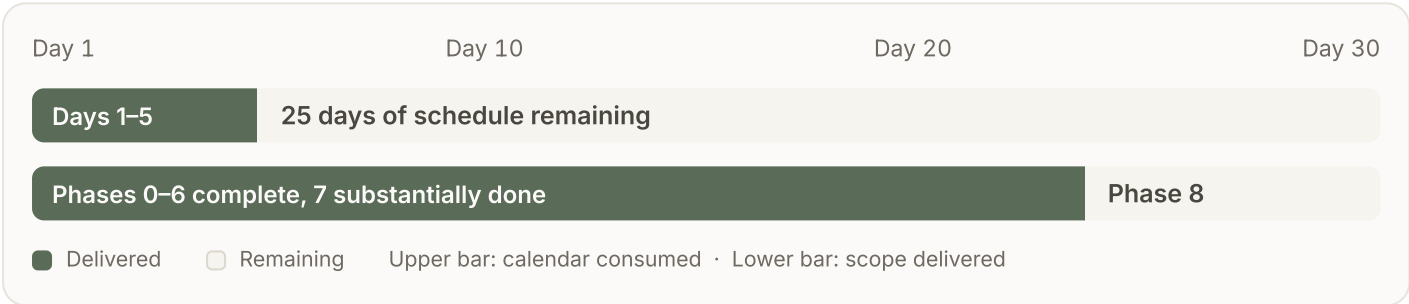

Read the two bars against each other: we have spent 17% of the days and delivered 78% of the planned build. The gap between them is the schedule we have bought back.

DAILY THROUGHPUT

How fast, day by day

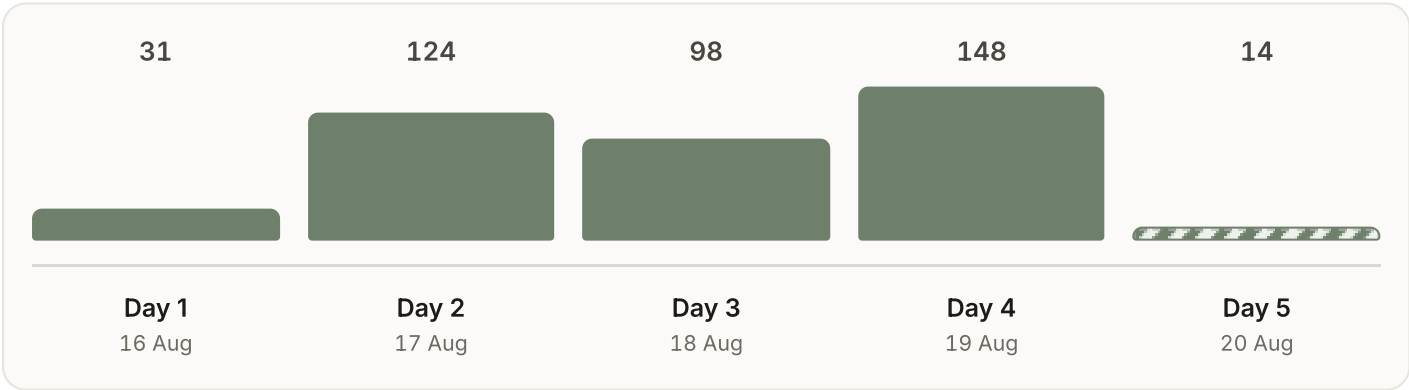

Changes committed per day, 415 in total. Day 5 (hatched) is partial — that day went to integration, verification and a working demo rather than new code, which is the shape you want at the end of a push. Four parallel work streams run simultaneously and are merged into one trunk daily.

Every phase, and when it landed

PHASE	LANDED	STATE
0 · Foundations Monorepo, design tokens, shared contract	Day 1	● Done
1 · Customer wallet Sign-in, signup, session layer, secure storage	Day 1–2	● Done
2 · Money core Charges, top-ups, voids, deposits, ledger	Day 2	● Done
3 · Staff scanner PIN, scan, charge, void, manual lookup	Day 2–3	● Done
4 · Merchant dashboard Nine sections, team authority, audit log	Day 3	● Done
5 · Shared platform state Promotions, happy hours, loyalty tiers	Day 3	● Done
6 · Booking and shop Appointments, deposits, product orders	Day 4	● Done
7 · Owner console Admins, approvals, policies, analytics, controls, audit, reports	Day 4–5	● Substantially done
8 · Hardening and launch Launch checklist: 15 of 53 items closed	Day 5 →	● In progress

DELIVERED

What exists and runs today

111 API endpoints

- 37 database migrations
- Money held as integer fils — no floating point anywhere
- Negative balances impossible at the database level

40 Screens

- Customer wallet — 7 screens
- Staff scanner — 11 screens
- Dashboard & owner console — 22 routes

889 Automated tests

- Run against real Postgres, not mocks
- Every money path tested under concurrency
- All 57 permission gates probed automatically

12 Non-negotiables

- All twelve satisfied and held by tests
- Full Arabic right-to-left layout
- Passwords never stored or shown in plain text

A working demo is available now

The merchant dashboard and owner console run end to end against a real database with seeded salons, staff and customers — sign-in, appointments, team permissions, loyalty, marketing, audit log, reports and CSV export. Roughly ten minutes to walk through.

What is blocking launch is no longer code

Fourteen open items need an AVO decision

Each is recorded with its reasoning and a safe default already shipped, so nothing is stalled today. But several have lead times measured in weeks, and they are now the long pole. The four with the longest lead are below.

- 1

Central Bank position on holding stored value
Does AVO holding customer balances need its own licence? Our payment provider being licensed answers who *moves* money, not who may *hold* it. Regulatory, and the single largest launch risk.
- 2

Legal sign-off on the policy set
Seven documents are written, versioned and served to the apps, each carrying “awaiting counsel and payment-provider sign-off”. Seeding the text is not approval of it.
- 3

WhatsApp templates and a sending domain
Receipts, reset links and campaigns are fully built behind a logging driver — the queue, retries and de-duplication all work. Nothing can actually send until templates are approved.
- 4

Arabic review by a native speaker
74 strings have no Arabic source in the design bundle. They are tracked and deliberately left in English rather than machine-translated; a wrong register in a women’s salon product is a defect. The list is ready as a worksheet.

Also outstanding and lower risk: one hour with a physical phone to prove a live QR charge (the simulator has no camera), a decision on data residency, and who staffs the support queue and in what hours.

ASSESSMENT

Where this lands

On engineering alone, this build would be launch-ready well inside the 30 days. The realistic launch date is now set by the regulatory answer and the legal review, not by remaining development. The most valuable thing that can happen this week is starting items 1 and 2 — both have external lead times, and both can run in parallel with the hardening work already underway.
